




Alaskan Way Viaduct & Seawall Replacement Program

Case 2:09-cv-01305-JCC Document 33-15 Filed 05/08/2010 Page 1 of 2
 The Alaskan Way Viaduct and Seawall Replacement Program includes multiple projects that have independent utility. These graphics are designed to show different stages of construction to replace the south end of the viaduct. Separate construction contracts and projects have been combined for clarity of presentation.



Proposed South End Viaduct Replacement Construction Staging Concept: August 2013 - December 2015

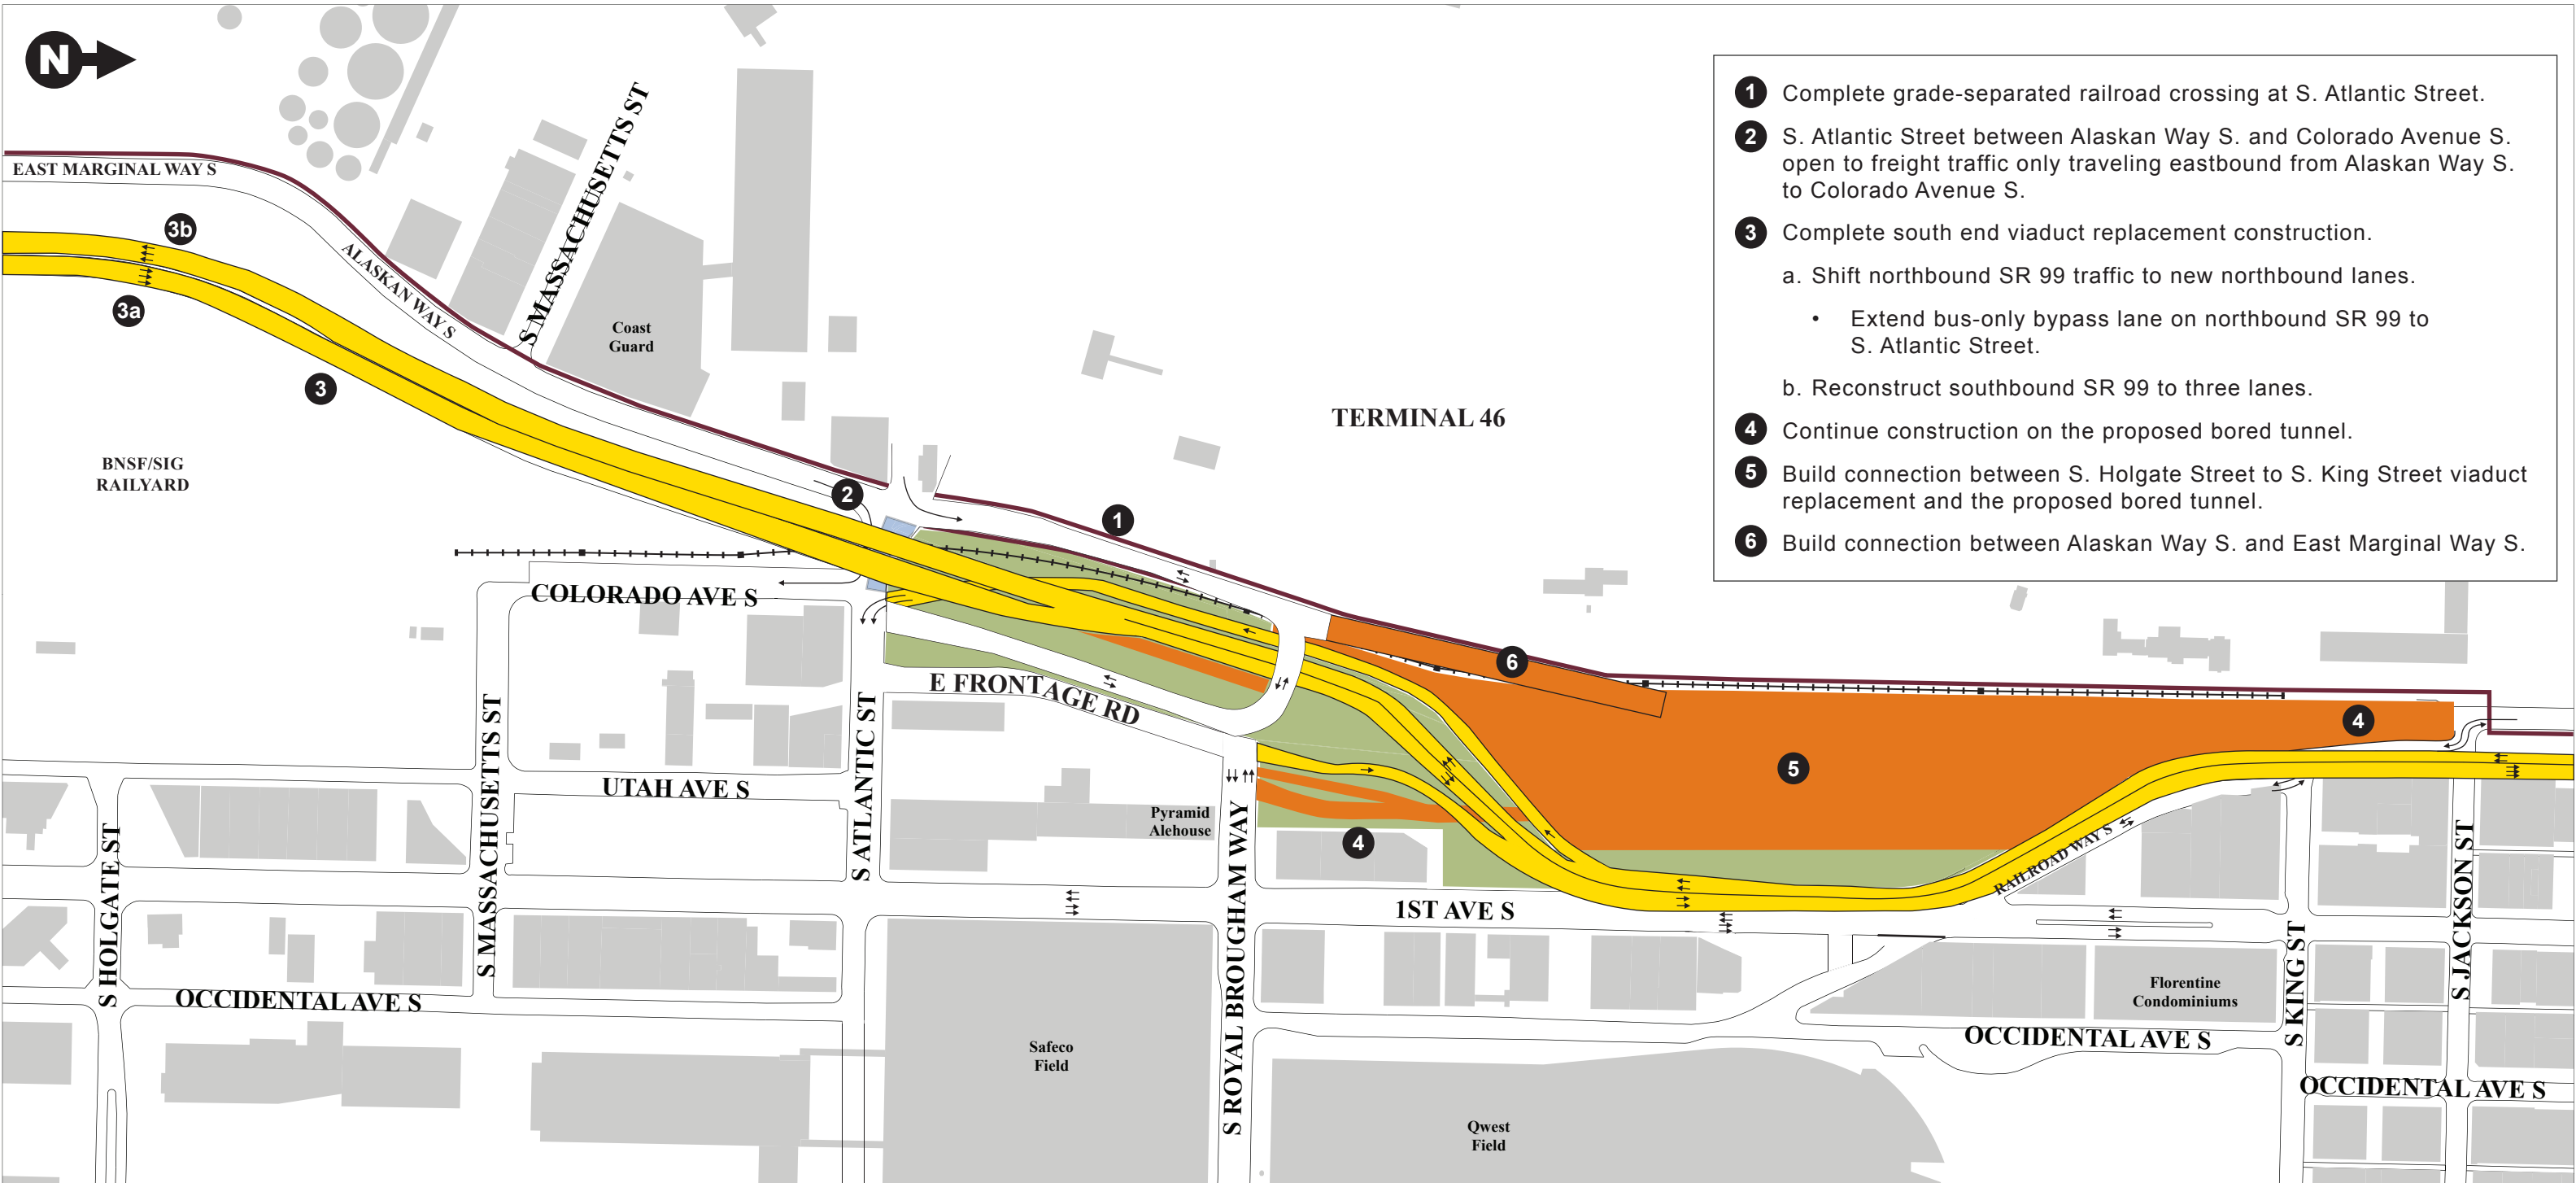

- 1 Complete grade-separated railroad crossing at S. Atlantic Street.
- 2 S. Atlantic Street between Alaskan Way S. and Colorado Avenue S. open to freight traffic only traveling eastbound from Alaskan Way S. to Colorado Avenue S.
- 3 Complete south end viaduct replacement construction.
 - a. Shift northbound SR 99 traffic to new northbound lanes.
 - Extend bus-only bypass lane on northbound SR 99 to S. Atlantic Street.
 - b. Reconstruct southbound SR 99 to three lanes.
- 4 Continue construction on the proposed bored tunnel.
- 5 Build connection between S. Holgate Street to S. King Street viaduct replacement and the proposed bored tunnel.
- 6 Build connection between Alaskan Way S. and East Marginal Way S.

Legend Construction area Staging area Open to SR 99 traffic Full vehicle traffic closure Intermittent/partial traffic closure Bike/ped path ***DRAFT SUBJECT TO CHANGE***

2010				2011				2012				2013				2014				2015			
Winter	Spring	Summer	Fall	Winter	Spring	Summer	Fall	Winter	Spring	Summer	Fall	Winter	Spring	Summer	Fall	Winter	Spring	Summer	Fall	Winter	Spring	Summer	Fall




Alaskan Way Viaduct & Seawall Replacement Program

Case 2:09-cv-01305-JCC Document 33-15 Filed 05/08/2010 Page 2 of 2
 The Alaskan Way Viaduct and Seawall Replacement Program includes multiple projects that have independent utility. These graphics are designed to show different stages of construction to replace the south end of the viaduct. Separate construction contracts and projects have been combined for clarity of presentation.



Proposed South End Viaduct Replacement Construction Staging Concept: 2016 - 2017

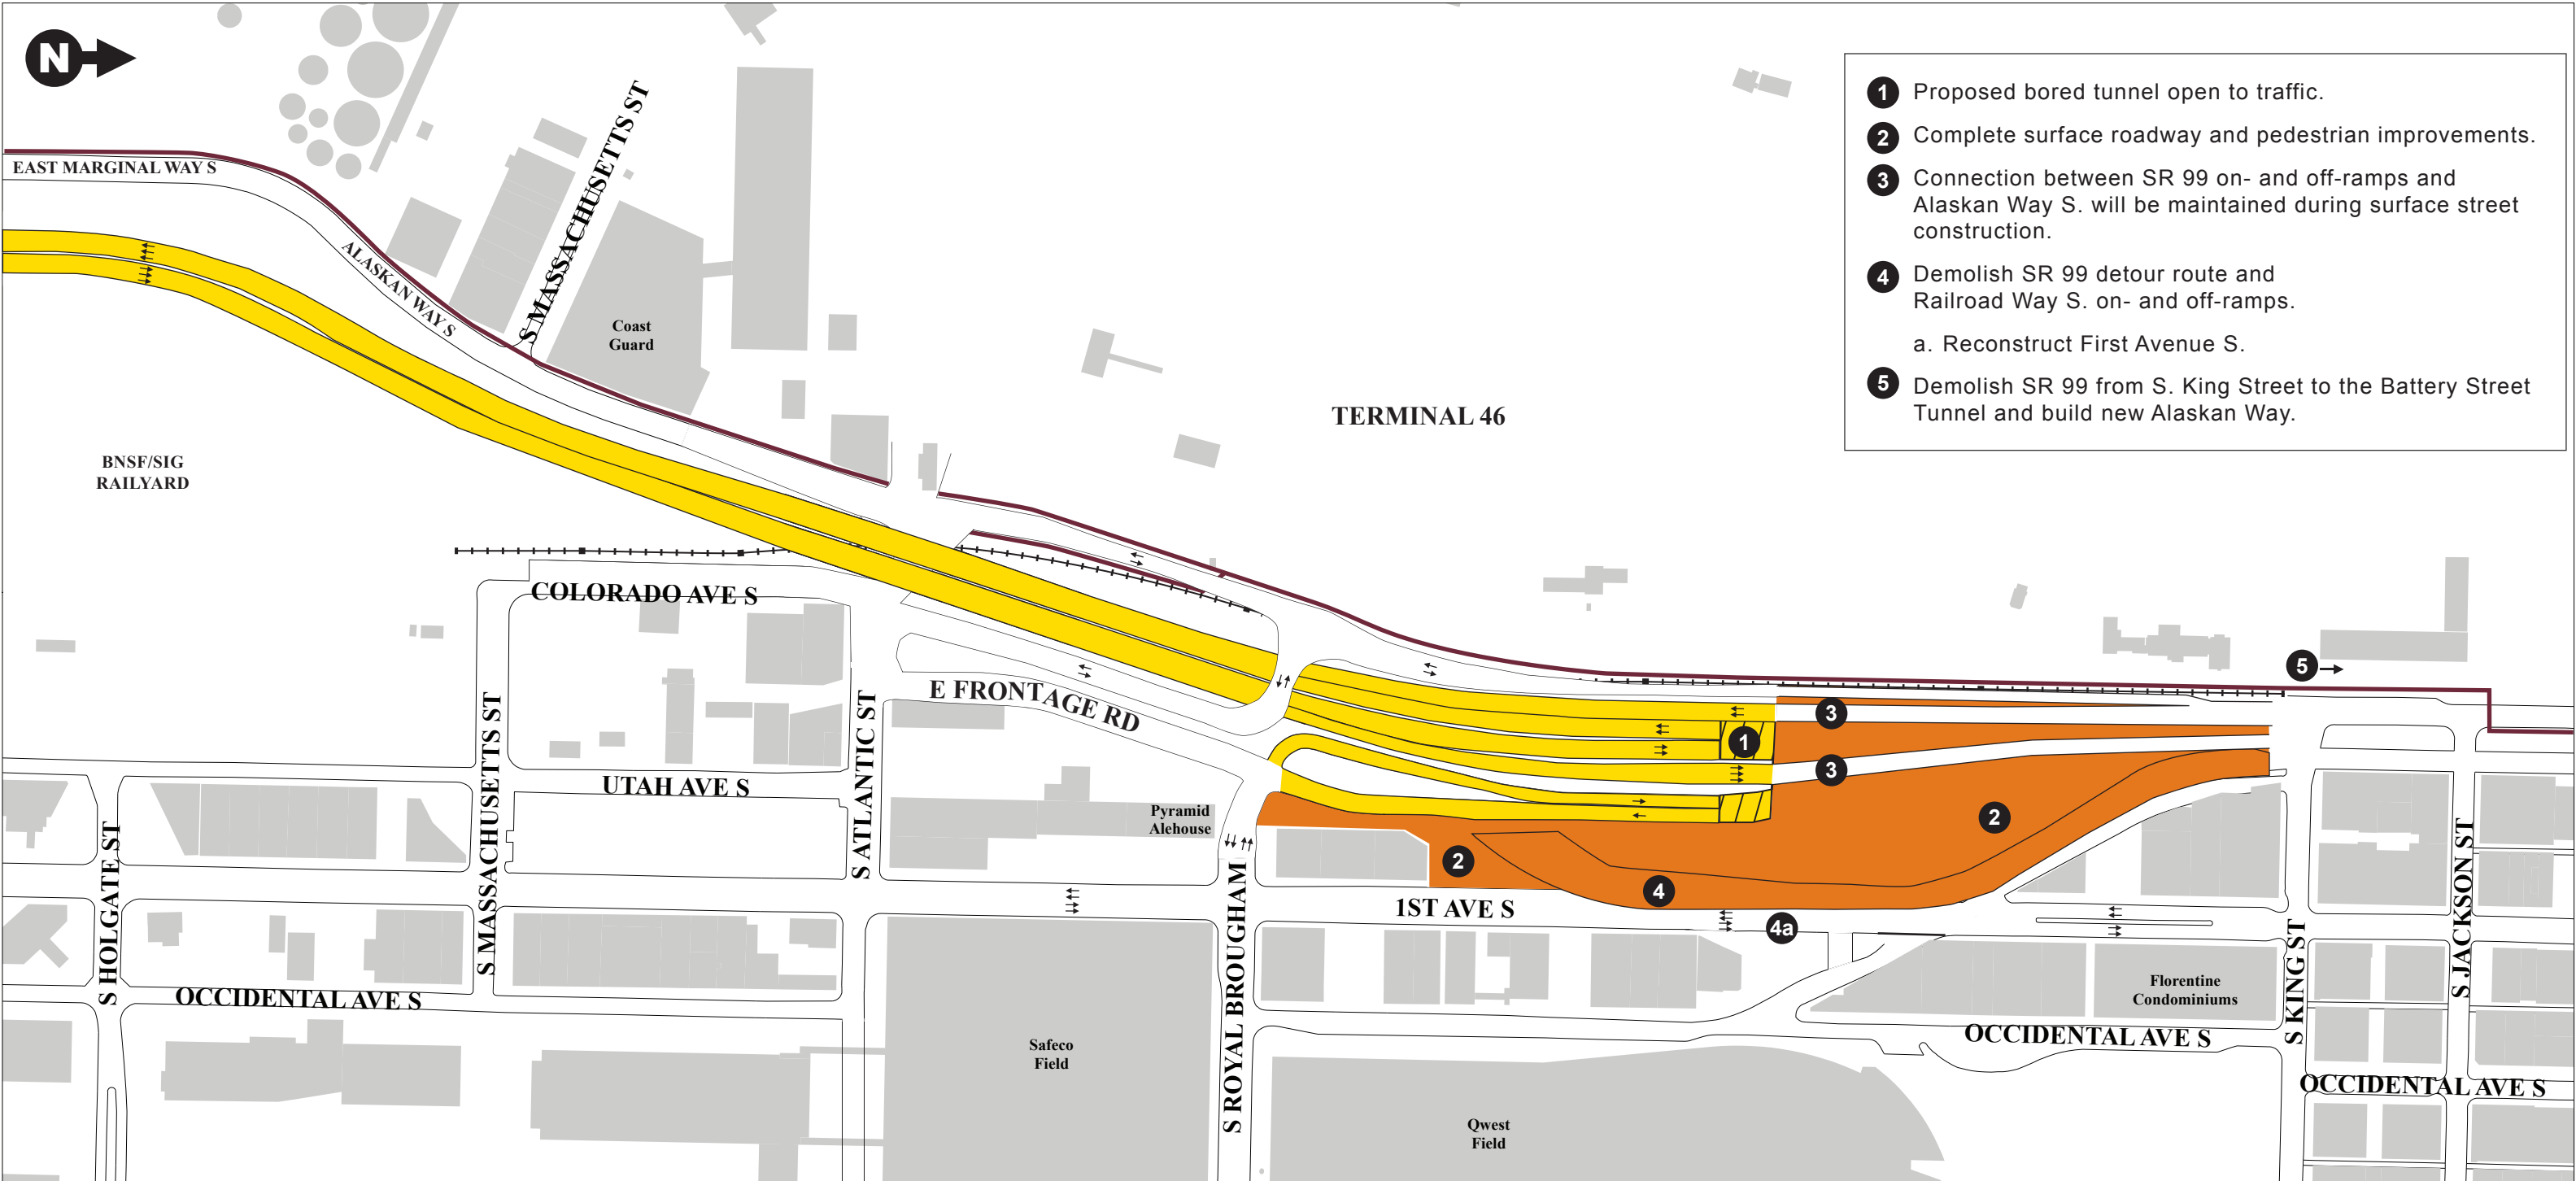

- 1 Proposed bored tunnel open to traffic.
- 2 Complete surface roadway and pedestrian improvements.
- 3 Connection between SR 99 on- and off-ramps and Alaskan Way S. will be maintained during surface street construction.
- 4 Demolish SR 99 detour route and Railroad Way S. on- and off-ramps.
 - a. Reconstruct First Avenue S.
- 5 Demolish SR 99 from S. King Street to the Battery Street Tunnel and build new Alaskan Way.

Legend: Construction area (orange), Open to SR 99 traffic (yellow), Proposed bored tunnel (hatched), Bike/ped path (dark red). ***DRAFT SUBJECT TO CHANGE***

2011				2012				2013				2014				2015				2016			
Winter	Spring	Summer	Fall	Winter	Spring	Summer	Fall	Winter	Spring	Summer	Fall	Winter	Spring	Summer	Fall	Winter	Spring	Summer	Fall	Winter	Spring	Summer	Fall
